


E2E Data & Integration

WAYS OF WORKING

JANUARY 2024



Team and Structure

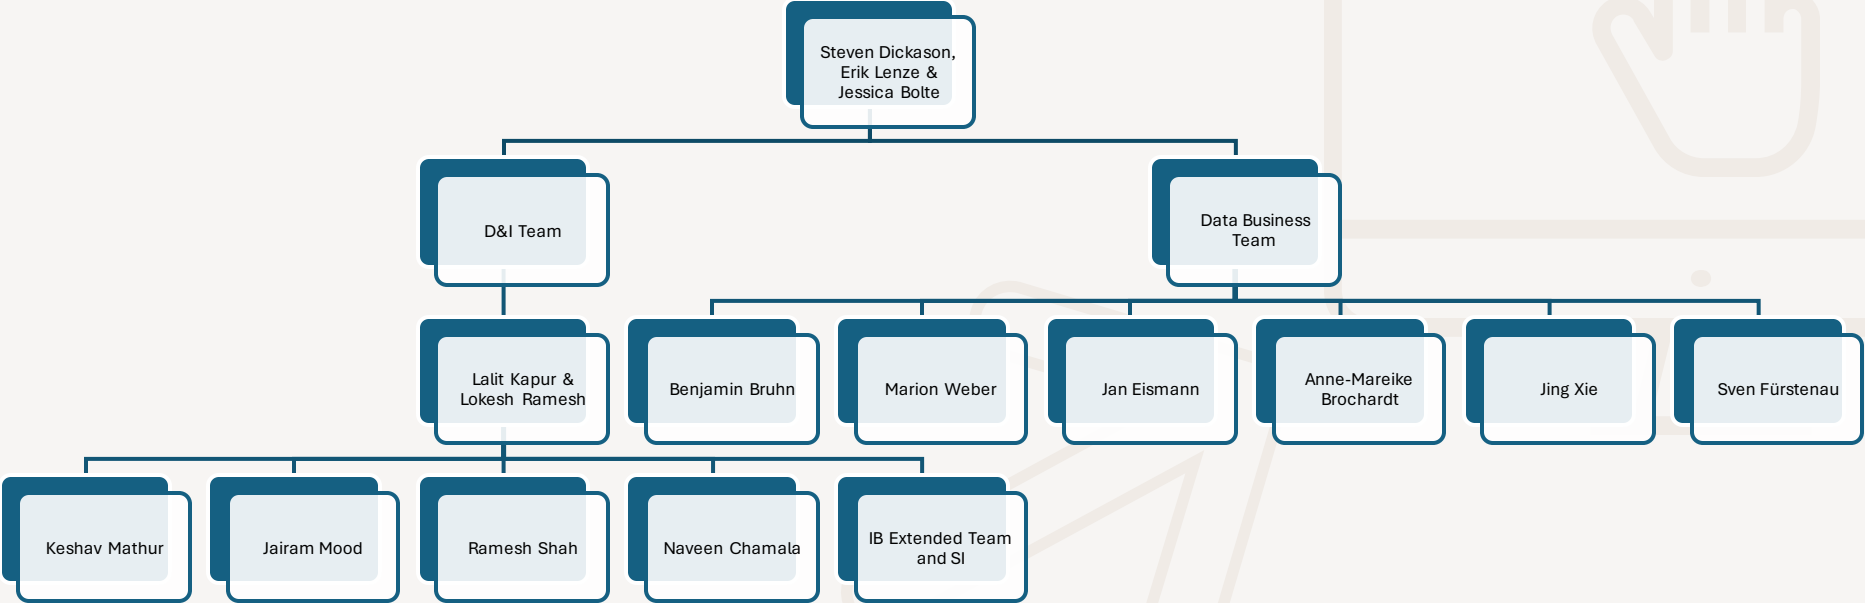

Data & Integration Milestone Activities

[Link: E2E Data and Integration Milestones PLAN.xlsx](#)

Global Template Data and Integration (D&I) Design to connect the Source and Target systems for connecting to E2E Supply Chain Planning solution (Blue Yonder) and Forecasting tool Noodle.

Design/ Build/ Testing/ Cutover/ Go-Live support for Data Hub solution for:


DP (Demand Planning)

DRP/Supply Unify

DRP Legacy APO

Noodle Wave#2 and

Noodle Wave#3

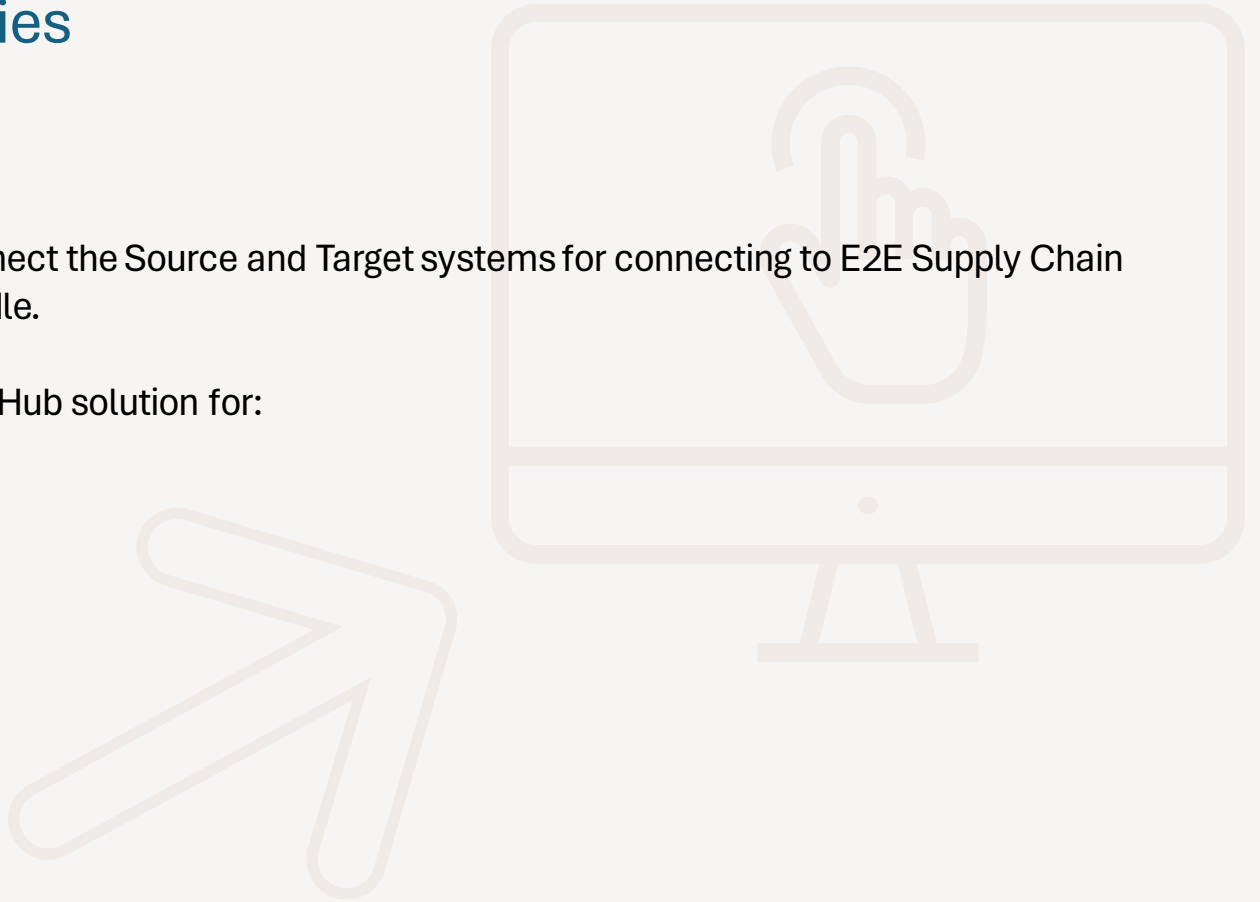

Data & Integration Datahub Weekly Updates

[Link: 07.1 E2E D&I Data Hub Weekly Updates](#)

Weekly updates (every Wed) for the previous week by the E2E D&I Team

- Include previous week key task with RAG and Status with Baseline and Forecast Date if delayed.
- Requirement / Development Log – key updates
- Deliverables status with progress % including Baseline and Forecast Date.
- Open Items

Risk and Issues raised and status.
Any escalations.


To monitor the progress of Datahub activities and address any issues impeding advancement. This communication ensures a comprehensive understanding of ongoing initiatives and facilitates the prompt resolution of challenges to maintain a smooth workflow.

Datahub Data Entities Requirement Documents

[Link: A02 E2E DATA HUB Data Entities RequirementDoc.xlsm](#)

Details requirement of DATA Entities for Master Data, Transaction Data, Outbound Data for below Blue yonder Modules :

DP	9 Data Entities
DRP	28 Data Entities (TBC)
Supply	24 Data Entities (TBC)

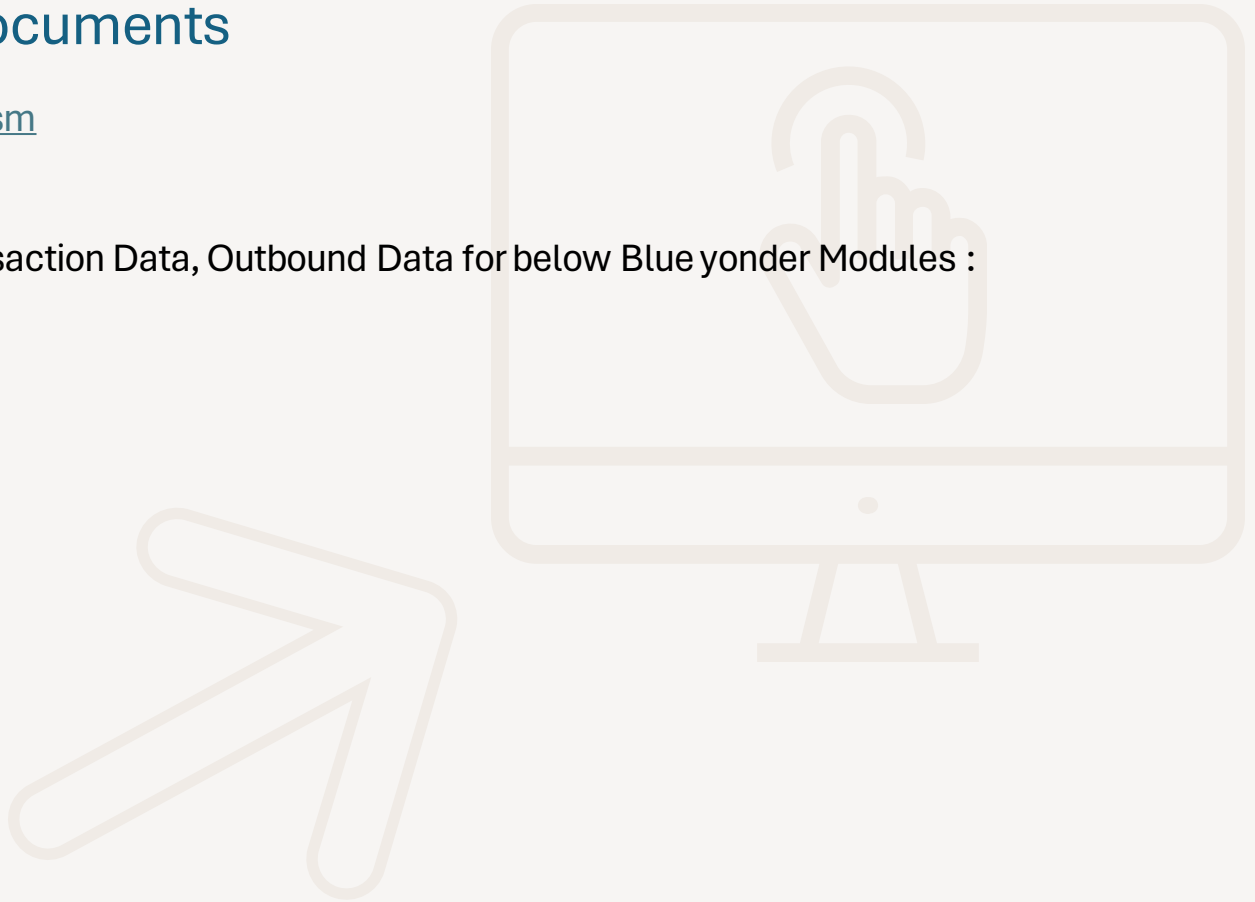


Data Requirement Development Tracking Log

[Link: E2E DATA HUB Requirement Development Tracking Log.xlsx](#)

Document to store and keep track on additional Requirement.


Requirement once approved moved to Development log. with DH requirement details along with owners, Next action and resolution date status.

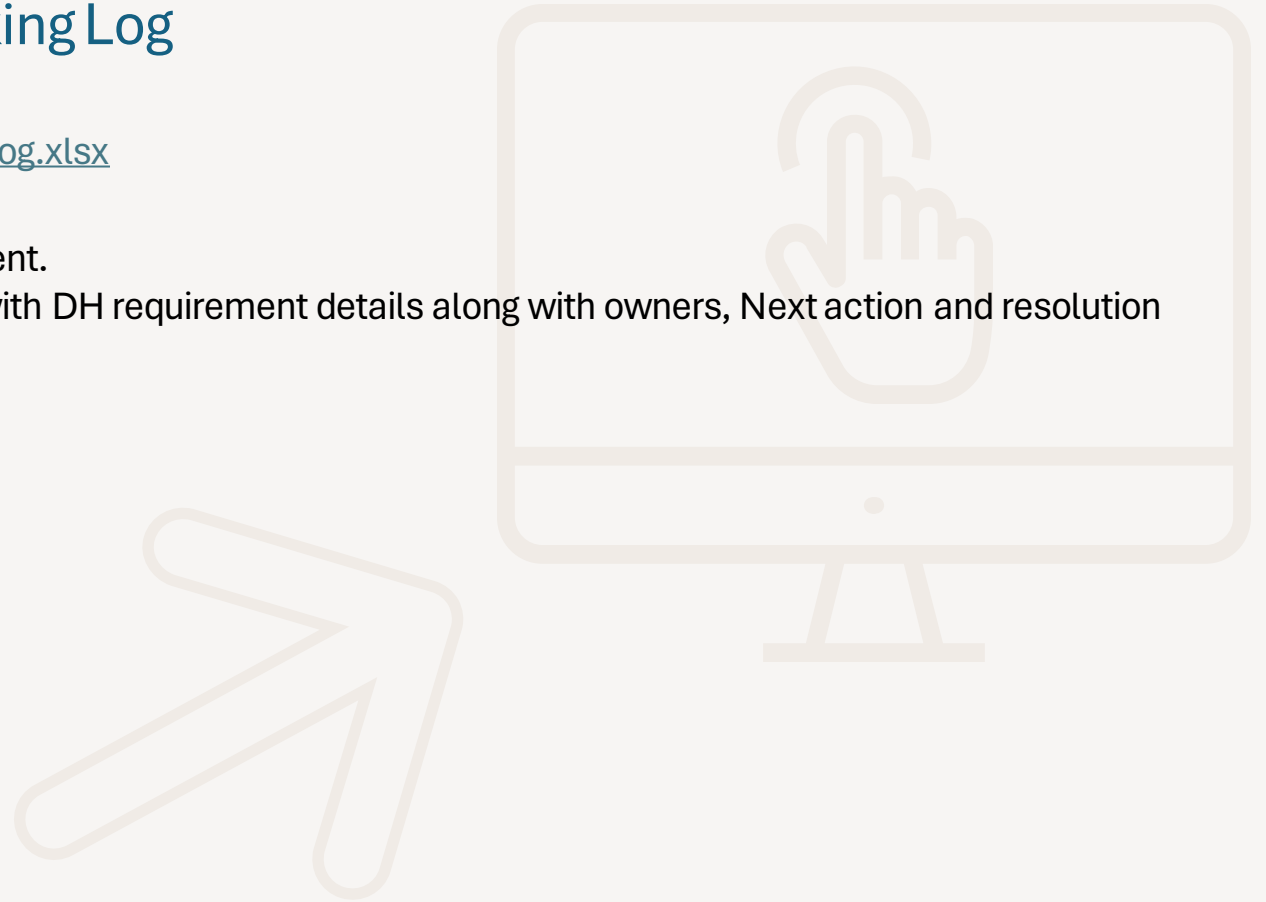

Data & Integration Datahub Deliverables

[Link: 07.4 E2E D&I Data Hub Deliverables](#)

All the Documents related to Datahub deliveries stays in this folder.

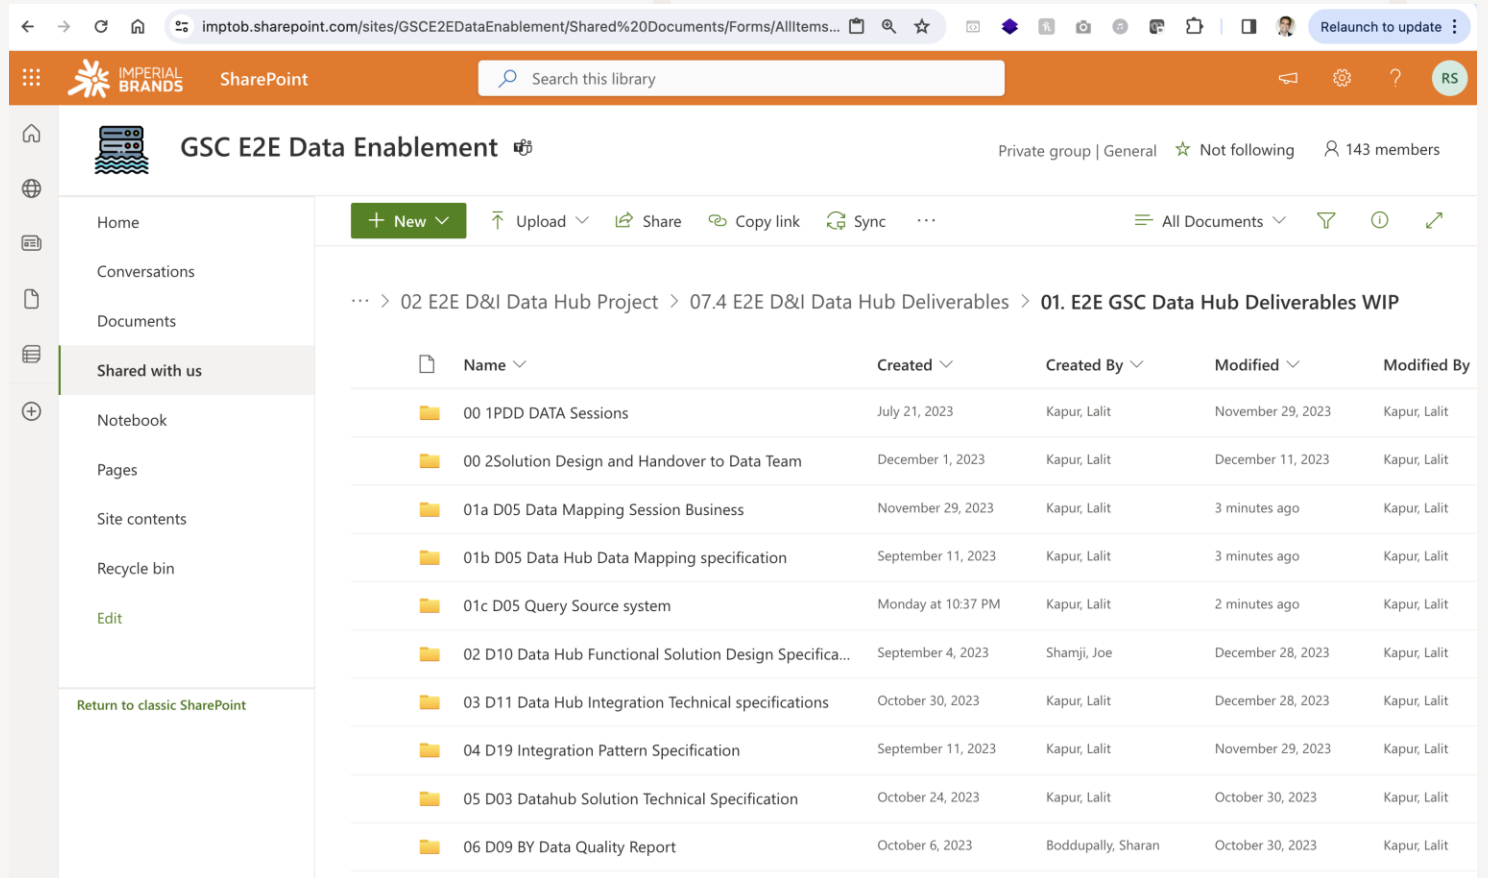

imptob.sharepoint.com/sites/GSCE2EDataEnablement/Shared%20Documents/Forms/AllItems...

SharePoint

Search this library

Relaunch to update

IMPERIAL BRANDS

GSC E2E Data Enablement

Private group | General ☆ Not following 143 members

+ New Upload Share Copy link Sync

All Documents

02 E2E D&I Data Hub Project > 07.4 E2E D&I Data Hub Deliverables > 01. E2E GSC Data Hub Deliverables WIP


Name	Created	Created By	Modified	Modified By
00 1PDD DATA Sessions	July 21, 2023	Kapur, Lalit	November 29, 2023	Kapur, Lalit
00 2Solution Design and Handover to Data Team	December 1, 2023	Kapur, Lalit	December 11, 2023	Kapur, Lalit
01a D05 Data Mapping Session Business	November 29, 2023	Kapur, Lalit	3 minutes ago	Kapur, Lalit
01b D05 Data Hub Data Mapping specification	September 11, 2023	Kapur, Lalit	3 minutes ago	Kapur, Lalit
01c D05 Query Source system	Monday at 10:37 PM	Kapur, Lalit	2 minutes ago	Kapur, Lalit
02 D10 Data Hub Functional Solution Design Specifica...	September 4, 2023	Shamji, Joe	December 28, 2023	Kapur, Lalit
03 D11 Data Hub Integration Technical specifications	October 30, 2023	Kapur, Lalit	December 28, 2023	Kapur, Lalit
04 D19 Integration Pattern Specification	September 11, 2023	Kapur, Lalit	November 29, 2023	Kapur, Lalit
05 D03 Datahub Solution Technical Specification	October 24, 2023	Kapur, Lalit	October 30, 2023	Kapur, Lalit
06 D09 BY Data Quality Report	October 6, 2023	Boddupally, Sharan	October 30, 2023	Kapur, Lalit

Return to classic SharePoint

Data & Integration Team Tracker IB Internal Team IT

[Link: 07.5a E2E D&I TEAMTRACKER IB Internal Team IT](#)

SI Teams (D&I POD1 and D&I POD2) to plan the weekly deliverables.

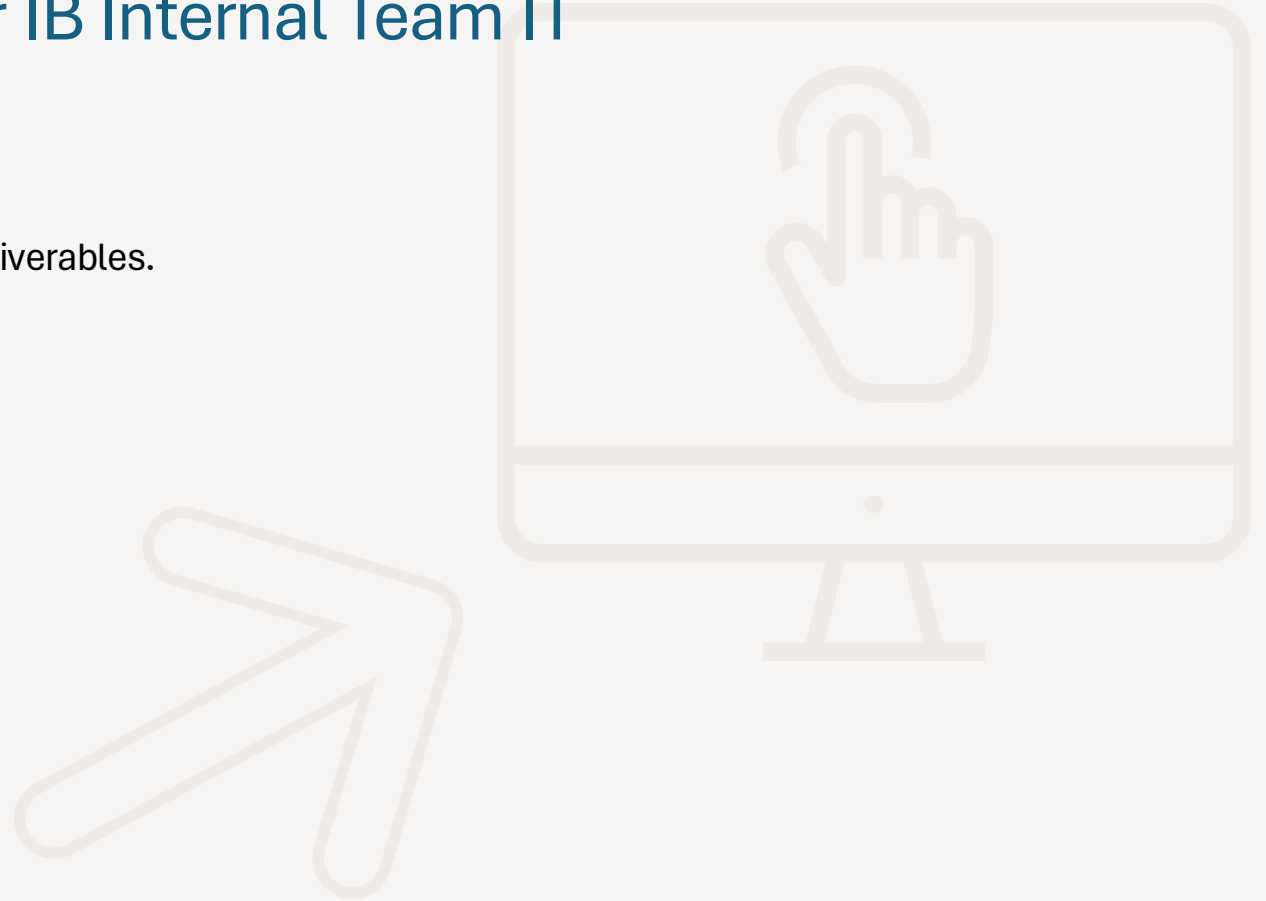

Data & Integration Team Tracker IB Internal Team Business

[Link: 07.5b E2E D&I TEAM TRACKER IB Internal Team Business](#)

Details of Business activities can be tracked here.

Introduction to new SI – LTI Mindtree

Sr. No	Name	POD # A/B/C	Role
1	Sayak Deb	Delivery Manager	Delivery Manager
2	Abhijith NV	Practice Lead	Practice Lead
3	Nitin Pateria	Program Director	Program Director
4	Krishna Mohan Rao Kaluri	Lighthouse	Program Manager
5	Sumanta Dutta	Lighthouse	Technical Architect
6	Angshuman Biswas	Lighthouse	Program Manager
7	Surajit Samanta	Lighthouse	Supply Chain Consultant
8	Suresh Babu K	Lighthouse	Data Architect
9	Ritabrata Sanyal	Lighthouse	BY Engineer
10	Harikrishnan Maheswaran	D&I POD#2	Data Tech Project Manager
11	Sneha Yeallinki	D&I POD#2	Data Analyst
12	Kishore Kumar S	D&I POD#2	Functional Consultant
13	Umamaheswara Mule	D&I POD#2	Modern Data Sr. Technical Lead
14	Syed Hussain	D&I POD#2	Modern Data Technical Lead
15	Erramilli Sessa Venkata Sriram	D&I POD#2	Integration Lead
16	Arun KS	D&I POD#2	Modern Data Technical Lead
17	Sachin Hosangadi	D&I POD#2	Sr Test Lead
18	Jayachandiran Ravichandran	D&I POD#1	Functional Consultant
19	Hemant Meenanath Patil	D&I POD#1	Modern Data Sr. Technical Lead
20	Nabendu Roy	D&I POD#1	Modern Data Technical Lead
21	Chandrashi Shivkumar Tiwari	D&I POD#1	Test Engineer

Process of Data Entity Flow

Responsible, Accountable, Consulted & Informed

Sr No.	Details/Documents	D&I - IT	D&I - Business
1	Handover of Data Entities to D&I team from BY Solution Design Team	R, A	C
2	D&I Team internal alignment on data entities	R, A	-
3	Mapping sessions with Source System Functional Design Owners	R, A	C
4	D05 Data Hub Data Mapping specification	R, A	C
5	D10 Data Hub Functional Solution Design Specifications	R, A	I
6	D11 Data Hub Integration Technical specifications	R, A	I
7	D19 Integration Pattern Specification	R, A	I
8	D03 Datahub Solution Technical Specification	R, A	-
9	D09 BY Data Quality Report	R, A	C
